

PROJECT UPDATE

February 2026



CA0604

Main Street to Vandenberg Boulevard



Construction Overview



Started April 2023



Widening 2.5 miles of Hwy. 67/167 (I-57) to 6 lanes (Main St. - Vandenberg Blvd.)



Overpasses and bridges
- James St. replacement
- Gregory St. new structure
- Vandenberg Blvd. replacement



Ramp alignment improvements



Frontage roads converted to one-way (Main St. - Vandenberg Blvd.)



Estimated completion late 2026



Highlights

Gregory Street Bridge opened to the public February 2026.

The old **northbound Vandenberg Blvd. Bridge** was demolished and new bridge construction was started (*see picture below*).

Traffic signals installed at the **Vandenberg Blvd. / John Harden Dr.** intersection.

Additional project photos are available on the project website (scan the QR code or see link in footer).



Recent Work

- Vandenberg Boulevard Bridge work
- Gregory Street overpass work
- Barrier wall, median, and drainage work in various locations
- Paving in various locations
- Highway 67/167 (I-57) main lane construction
- Frontage road and ramp work in various locations
- Traffic signal work at various intersections
- Earthwork along Hwy. 67/167 (I-57)


Construction Progress

83%



Look Ahead*

- Continued northbound Vandenberg Blvd. Bridge construction
- Paving Hwy. 67/167 (I-57) northbound mainlanes

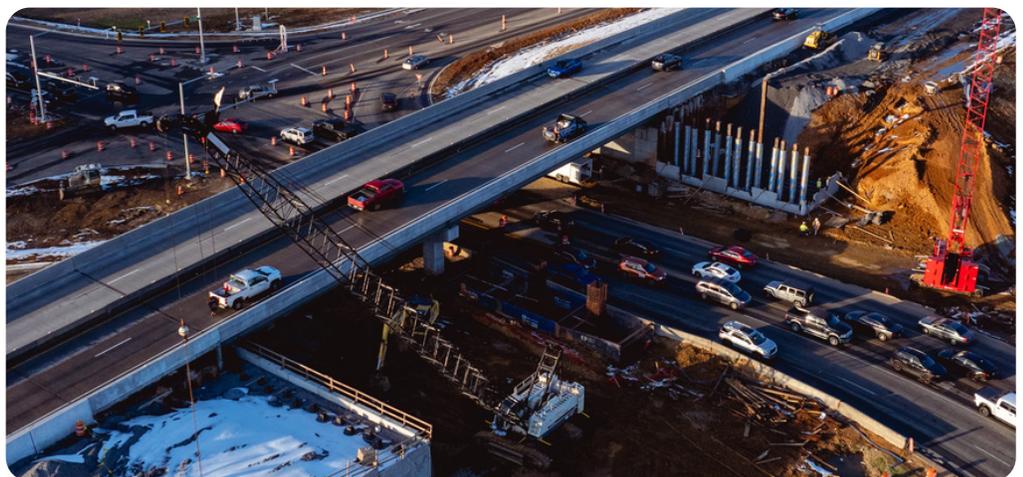

NB Highway 67/167 (I-57) new Vandenberg Blvd. Bridge construction

*Preliminary schedule subject to change



• Phone: 501-255-1519

• Email: info@ConnectingArkansasProgram.com

• Project Website: ConnectingArkansasProgram.com

